Draft Schedule - MC7B

Data Date = 01NOV09

Run Date of Schedule:
16NOV09 15:24

DRAFT
MPC Construction Schedules
For Approval

Schedule
Date Date
01NOV09

Building Construction Sequences
1. 16-->02-->10-->15-->03
2. NSS---->29 & 04 --->07
3. 27--->21N --->21S-->19
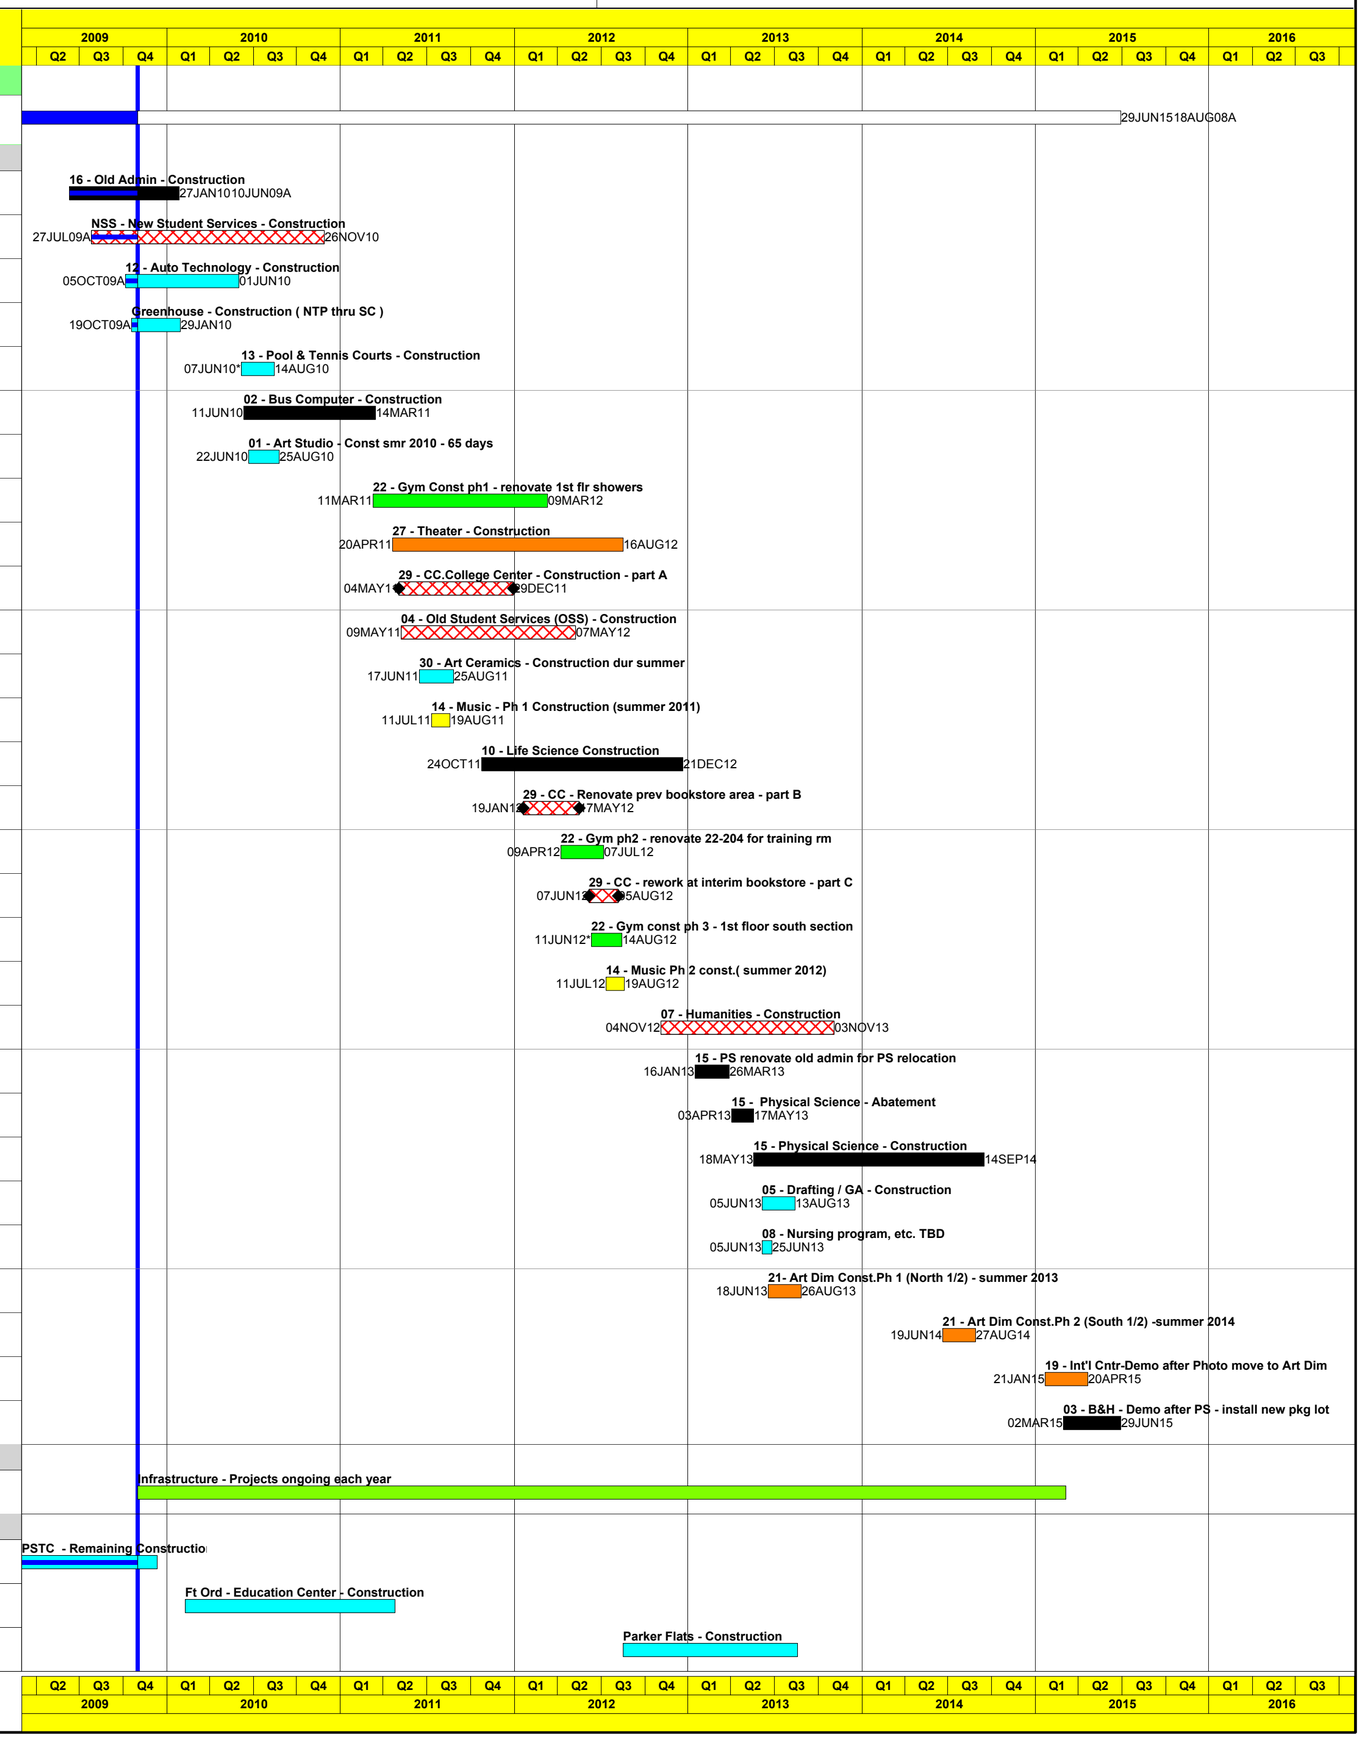
Activity ID	Activity Description	Const Dur	Const Start	Const Finish
MPC Project Sched - option 7B				
Total		2,507	18AUG08A	29JUN15
MPC - Building Projects				
16-CNST	16 - Old Admin - Construction	232	10JUN09A	27JAN10
NSS-CNST	NSS - New Student Services - Construction	488	27JUL09A	26NOV10
12-CNST	12 - Auto Technology - Construction	240	05OCT09A	01JUN10
52-CNST	Greenhouse - Construction (NTP thru SC)	102	19OCT09A	29JAN10
13-CNST	13 - Pool & Tennis Courts - Construction	69	07JUN10*	14AUG10
02-CNST	02 - Bus Computer - Construction	277	11JUN10	14MAR11
01-CNST	01 - Art Studio - Const smr 2010 - 65 days	65	22JUN10	25AUG10
22-CNST.1	22 - Gym Const ph1 - renovate 1st flr showers	365	11MAR11	09MAR12
27-CNST	27 - Theater - Construction	485	20APR11	16AUG12
29-CNST.1	29 - CC.College Center - Construction - part A	240	04MAY11	29DEC11
04-CNST	04 - Old Student Services (OSS) - Construction	365	09MAY11	07MAY12
30-CNST	30 - Art Ceramics - Construction dur summer	70	17JUN11	25AUG11
14-CNST.1	14 - Music - Ph 1 Construction (summer 2011)	40	11JUL11	19AUG11
10-CNST.2	10 - Life Science Construction	425	24OCT11	21DEC12
29-CNST.2	29 - CC - Renovate prev bookstore area - part B	120	19JAN12	17MAY12
22-CNST.2	22 - Gym ph2 - renovate 22-204 for training rm	90	09APR12	07JUL12
29-CNST.3	29 - CC - rework at interim bookstore - part C	60	07JUN12	05AUG12
22-CNST.3	22 - Gym const ph 3 - 1st floor south section	65	11JUN12*	14AUG12
14-CNST.2	14 - Music Ph 2 const.(summer 2012)	40	11JUL12	19AUG12
07-CNST	07 - Humanities - Construction	365	04NOV12	03NOV13
15-SS	15 - PS renovate old admin for PS relocation	70	16JAN13	26MAR13
15-HAZ	15 - Physical Science - Abatement	45	03APR13	17MAY13
15-CNST	15 - Physical Science - Construction	485	18MAY13	14SEP14
05-CNST	05 - Drafting / GA - Construction	70	05JUN13	13AUG13
08-DSN	08 - Nursing program, etc. TBD	21	05JUN13	25JUN13
21-CNST.1	21- Art Dim Const.Ph 1 (North 1/2) - summer 2013	70	18JUN13	26AUG13
21-CNST.2	21 - Art Dim Const.Ph 2 (South 1/2) -summer 2014	70	19JUN14	27AUG14
19-DEMO	19 - Int'l Cntr-Demo after Photo move to Art Dim	90	21JAN15	20APR15
03-CNST	03 - B&H - Demo after PS - install new pkg lot	120	02MAR15	29JUN15
MPC Infrastructure Projects				
I-BDGT	Infrastructure - Projects ongoing each year	1,950	01NOV09	04MAR15
Ft Ord - Building Projects				
PSTC	PSTC - Remaining Construction	365	18AUG08A	10DEC09
EC-CNST	Ft Ord - Education Center - Construction	440	09FEB10	24APR11
PF-CNST	Parker Flats - Construction	365	18AUG12	17AUG13
